Project Title Mukwonago Pick 'N Save Pond

Start Date 5/12/2020
End Date 7/31/2020
Overall Progress

Tasks	Start	End	Days	Status	5/12	5/13	5/14	5/15	5/18	5/19	5/20	5/21	5/22
Preparation													
Mobilizaiton	13-May	26-May	9	In progress									
Traffic Sign Placement	13-May	13-May	1	Complete									
Barrier Fence	13-May	14-May	2	Complete									
Perimeter Control	13-May	18-May	2	95% - In progress									
Track Pad	18-May	19-May	1	Complete									
Inlet Sediment Guard	19-May	22-May	2	Not Started									
Excavation													
Clearing and grubbing	22-May	29-May	6	Not Started									
Remove riprap	22-May	29-May	6	Not Started									
Storm water facility dewatering	22-May	20-Jul	5	Not Started									
RCP prep & delivery	1-Jun	5-Jun	5	Not Started									
Storm sewer main, 48" RCP, w/ spoil backfill	1-Jun	5-Jun	5	Not Started									
Concrete storm sewer end sections, 48", w/end grate	1-Jun	5-Jun	5	Not Started									
Concrete storm sewer end sections, 72", w/end grate	1-Jun	5-Jun	5	Not Started									
Field stone level spreader	8-Jun	8-Jun	1	Not Started									
Heavy riprap	1-Jun	5-Jun	5	Not Started									
Storm water detention facility improvements,	8-Jun	20-Jul	6 weeks	Not Started									
Dust control using calcium chloride				Not Started									
Dust control using water (as needed)				Not Started									
Topsoil, native seeding and Class II, Type B erosion mat	8-Jun	27-Jul	6 weeks	Not Started									
, turf grass seeding, fertilizer and Class I, Urban, Type A erosi	8-Jun	27-Jul	6 weeks	Not Started									
Class III, Type B or C turf reinforcement	20-Jul	27-Jul	5	Not Started									
Phase 2													
Grading maintenance drive	20-Jul	27-Jul	5	Not Started									
Manufactured slope interruption device	15-May	20-May	4	95% - In Progress									
Topsoil, native seeding and class II, type B erosion mat	8-Jun	27-Jul	6 weeks	Not Started									

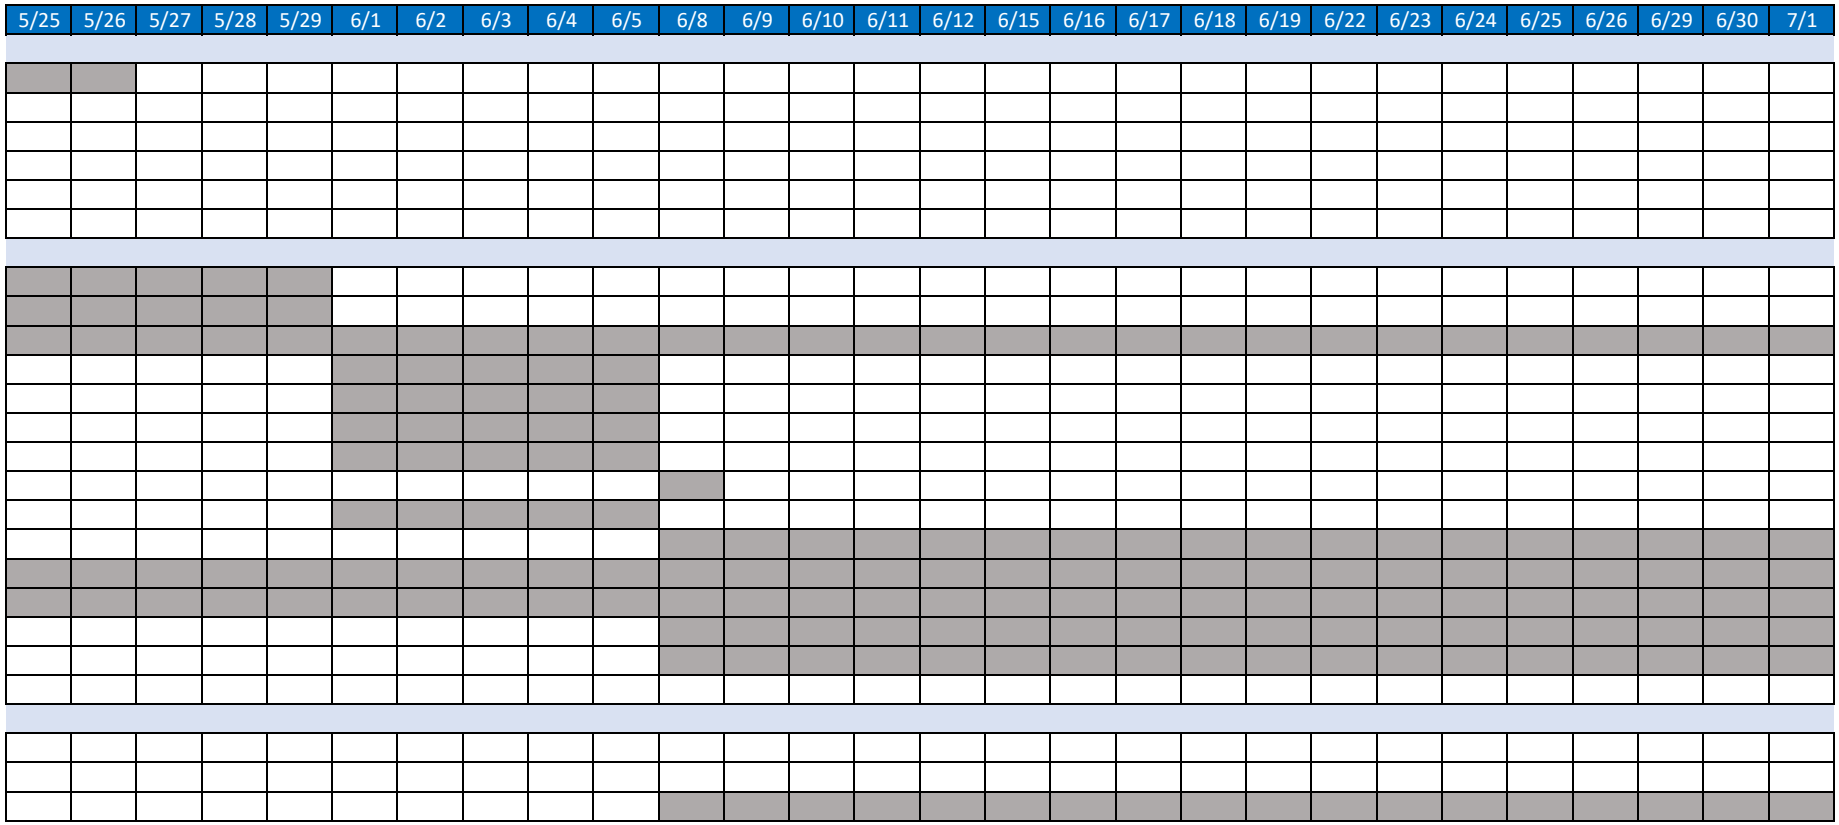
5/25
5/26
5/27
5/28
5/29
6/1
6/2
6/3
6/4
6/5
6/8
6/9
6/10
6/11
6/12
6/15
6/16
6/17
6/18
6/19
6/22
6/23
6/24
6/25
6/26
6/29
6/30
7/1

7/2	7/3	7/6	7/7	7/8	7/9	7/10	7/13	7/14	7/15	7/16	7/17	7/20	7/21	7/22	7/23	7/24	7/27	7/28	7/29	7/30	7/31
